BRHAT BANGALORE MAHANAGARA PALIKE

INSPECTION REPORT

Sl No	Decription	Details	Remarks
1	Name of Work	Improvements to Roads and Drains at Kattigenahalli Near Venkatesh House Road in Ward No.05 Byatarayanapura Sub Division	
2	Estimate Cost	12.00 Lakhs	
3	Administrative Approved No and Date	95/13-14, Date. 07.08.2013	
4	Technical sanction No. and Date	01/13-14, Date. 12.08.2013	
5	Job Code No. and P Code No.	005-13-000040	
6	Tender Direct Entrested to KRIDL	Nil	
7	if Tender, Tender Notification No. Date and Publication in daily news Paper		
8	Tender Approved Details		
9	Work Order No and Date	351/13-14, Date. 19.02.2014	
10	Stipulation time of Completion	60 Days	
11	Actiual Date of Commencement	01.07.2014	
12	Actiual Date of Completion	30.08.2014	
13	Delay if any	Nil	

	for Delay	Nil	
15	Payment made till date.	Nil	
16	Status of Work	Completed	
17	Photograph verfied	Enclosed	
18	Date of Inspection	26.05.2015	
19	MB No. and Page No.	Mb No. 1847 Page No. 184656 - 184664	
20	BR No. and Date	312/30.08.2014	
21	Test Result	Quality Test Report submitted by Karnataka Test House PVT Ltd is verified and Enclosed	
22	Section officer	Sri P A Chandrakanthraju A.E	
23	Sub Division Office	Sri Shivakumar Goudar AEE Byatarayanaprua Sub Division	
24	Observation		
a	Work Quality	Satisfactory	
b	Comments	Work completed as per MB	

Sd/- 26/05/15
(Y.C. Kale Gowda)
E.E (Retd)

Improvements to Roads and drains at Kattigenahalli near Venkatesh's house road in ward No-5 Byatarayapura Sub-division

ಸಹಾಯಕ ಅಭಿಯಂತರರು
ಬಿ.ಬಿ.ಎಂ.ಪಿ. ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ

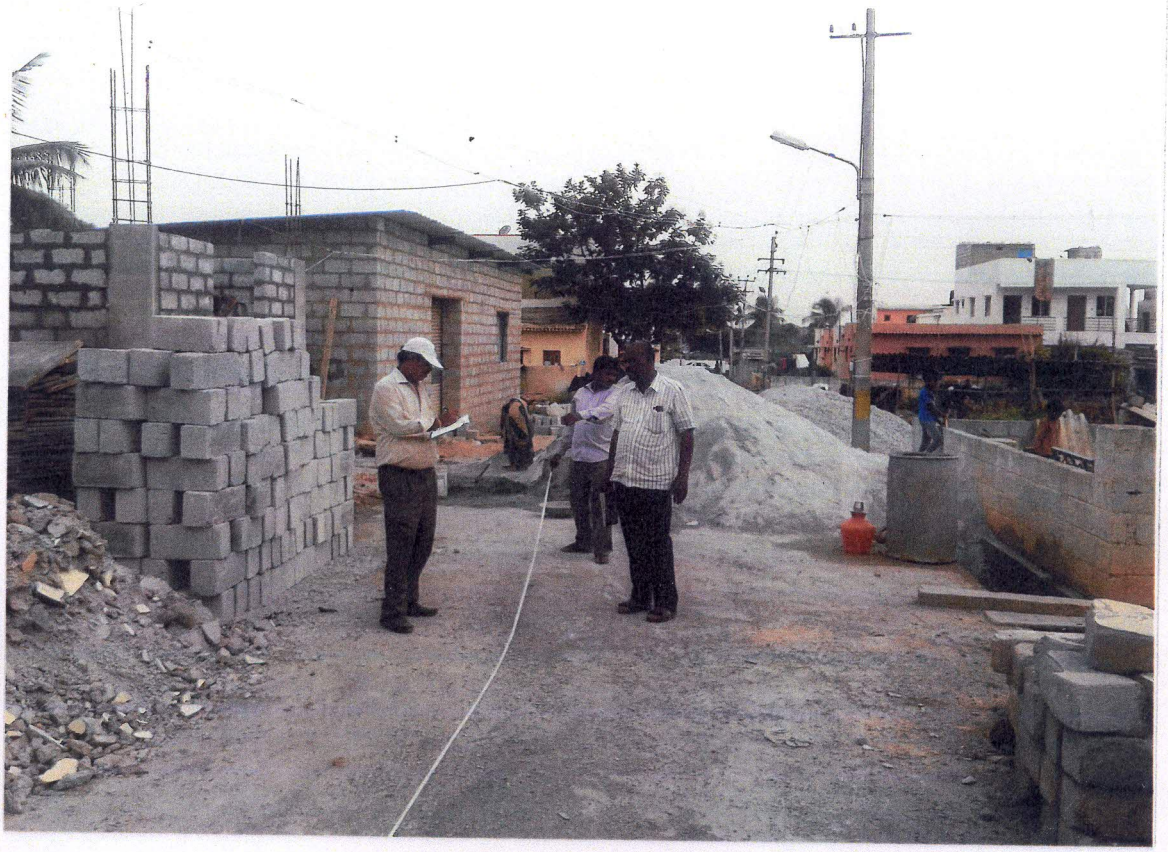

ಸಹಾಯಕ ಅಭಿಯಂತರರು

ಬಿ.ಬಿ.ಎಂ.ಪಿ, ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ
